



Executive Summary



The Deep Zone plant had 0 hours of Downtime during the 2nd week of April.

Ongoing Activities

Activities Completed This Week	Activities Planned (Anticipated Completion Date)
I&C Solutions continue to verify functionality of software for WIN 911 and XL Reporter (Apr 11 - 15) Conventional Well Sampling completed for 2015/2016 Annual/Semi-Annual Sample Event (Apr 11 - 15)	Conduct 2015/2016 Annual/Semi-Annual Sample Event Sample Westbay Wells (Apr 18 - 22) Meet with AMAFCA to discuss security issues to disable access to Tract 21 AMAFCA will line locate this week (Apr 4 - Apr 8) and install gates the following week.

Plant Operation Status

Wells	Weekly Average Rate - gpm	Design Rate - gpm	Total Flow - gallons	Design Flow - gallons	Percent Operational
EW-003R	219	250	2,207,800	2,520,000	88%
EW-004	139	140	1,401,120	1,411,200	99%
EW-005	107	100	1,078,560	1,008,000	107%
EW-006	125	100	1,260,000	1,008,000	125%
Total Flow	590	590	5,947,480	5,947,200	100%

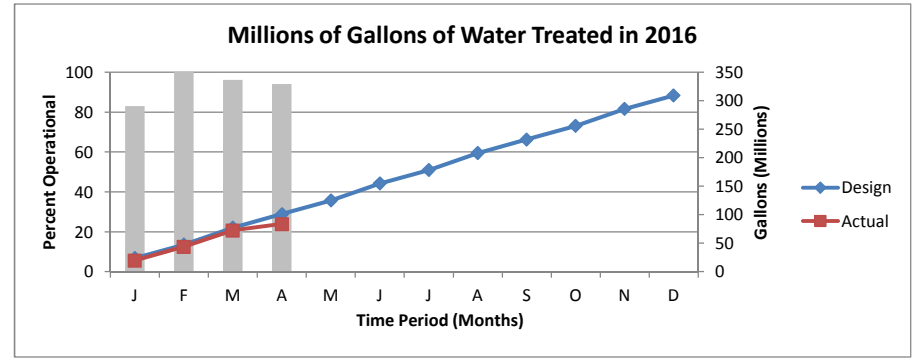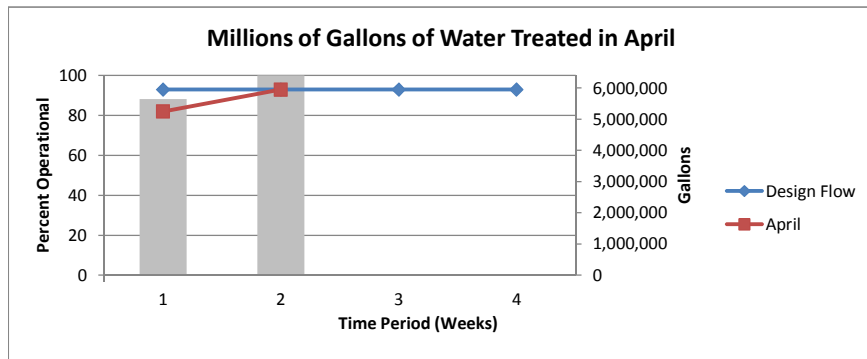

Plant Summary

The plant is processing 590 gpm and is operating with wells EW-004, EW-005, and EW-006 and EW-003R.

Year to Date:

	Monthly (2 week)	Yearly (15 week)
Design Flow (gallons) :	11,894,400	89,208,000
Actual Flow (gallons):	11,189,040	83,694,192
Percent of Design Flow:	94%	94%
Days Down:	32 hours	10 days 8 hours

Plant Repair Details:

I & C Solutions PLC Upgrade

On April 4, 2016, I & C Solutions staged the upgraded PLC at the Deep Zone Plant. On April 5, 2016 the Deep Zone Plant was shut down and the upgraded PLC installation began. On April 6, 2016 testing of the new PLC began the and the Plant was restarted. On April 12, 2016, software troubleshooting continued on Win 911 and and XL Reporter. The Plant has run without incident with the upgraded PLC.

Security:

Safety

On April 16, 2016 BCSO issued a LETTER OF NO TRESPASS to Jessica Ortega and Saul Mendoza

No Safety Incidents
No Near Misses
