AXIS GROUP INC AND RODGERS & COMPANY, INC
COMBINED DRILLING AND INSTALLATION SCHEDULE
EW-005, EW-006, & IW-636R

ID	Task Name	Duration	Duration	Start	Finish	Predecessors
1	**Axis - Rodgers Preconstruction Meeting**	1 day	1 day	Tue 12/2/14	Wed 12/3/14	
2	Site preparation, grubbing and clearing	1 day	1 day	Thu 12/4/14	Fri 12/5/14	
3	Install surface casing, move drilling rig and equipment	2 days	2 days	Thu 12/4/14	Sat 12/6/14	
4	Hazwopper training/refresher	3 days	3 days	Mon 12/8/14	Thu 12/11/14	2
5	**EW-005**	**22 days**	**22 days**	**Thu 12/11/14**	**Fri 1/2/15**	
6	Rig up driling rig, set mud pit	2 days	2 days	Thu 12/11/14	Sat 12/13/14	
7	Drill 17-1/2-in. production bore to 270 ft	4 days	4 days	Mon 12/15/14	Fri 12/19/14	6
8	Geophysical logs	0.5 days	0.5 days	Fri 12/19/14	Fri 12/19/14	7
9	Install well casing screen and annular materials	2 days	2 days	Sat 12/20/14	Mon 12/22/14	8
10	Well development, filter and transfer water	2 days	2 days	Mon 12/22/14	Wed 12/24/14	9
11	**Christmas Break**	**5 days**	**5 days**	**Wed 12/24/14**	**Mon 12/29/14**	10
12	Demobilize equipment, reclaim mud pit, and grade site	2 days	2 days	Mon 12/29/14	Wed 12/31/14	11
13	**New Years Eve New Years Day Break**	2 days	2 days	Wed 12/31/14	Fri 1/2/15	12
14	**EW-006**	**14 days**	**14 days**	**Fri 1/2/15**	**Fri 1/16/15**	
15	Rig up driling rig, set mud pit	1 day	1 day	Fri 1/2/15	Sat 1/3/15	13
16	Drill 17-1/2-in. production bore to 460 ft	6 days	6 days	Sat 1/3/15	Fri 1/9/15	15
17	Geophysical logs	0.5 days	0.5 days	Fri 1/9/15	Fri 1/9/15	16
18	Install well casing screen and annular materials	2 days	2 days	Sat 1/10/15	Mon 1/12/15	17
19	Well development, filter and transfer water	2 days	2 days	Mon 1/12/15	Wed 1/14/15	18
20	Demobilize equipment, reclaim mud pit, and grade site	2 days	2 days	Wed 1/14/15	Fri 1/16/15	19
21	**IW-636R**	**19 days**	**19 days**	**Fri 1/16/15**	**Wed 2/4/15**	20
22	Rig up driling rig, set mud pit	1 day	1 day	Fri 1/16/15	Sat 1/17/15	
23	Drill 17-1/2-in. production bore to 380 ft	5 days	5 days	Mon 1/19/15	Sat 1/24/15	22
24	Geophysical logs	0.5 days	0.5 days	Sat 1/24/15	Sat 1/24/15	23
25	Install well casing screen and annular materials	2 days	2 days	Sun 1/25/15	Tue 1/27/15	24
26	Well development, filter and transfer water	4 days	4 days	Tue 1/27/15	Sat 1/31/15	25
27	Demobilize equipment, reclaim mud pit, and grade site	2 days	2 days	Mon 2/2/15	Wed 2/4/15	26
28	**Connect the New Wells**	**84 days**	**84 days**	**Tue 12/2/14**	**Tue 2/24/15**	
29	Set Well Vaults by Rodgers	5 days	5 days	Wed 2/4/15	Mon 2/9/15	27
30	Utility Locates by Axis	14 days	14 days	Tue 12/2/14	Tue 12/16/14	
31	Obtain Quotations	20 days	20 days	Tue 12/16/14	Mon 1/5/15	30
32	Trench for New Water Lines and Electrical Conduits	10 days	10 days	Mon 1/5/15	Thu 1/15/15	31
33	Install Water Lines and Conduits from Electrical MH #1	10 days	10 days	Thu 1/15/15	Sun 1/25/15	32
34	Install Electrical	10 days	10 days	Sun 1/25/15	Wed 2/4/15	33
35	Install Level Sensors and Flow Meters	10 days	10 days	Wed 2/4/15	Sat 2/14/15	34
36	Startup and Commision Wells	10 days	10 days	Sat 2/14/15	Tue 2/24/15	35

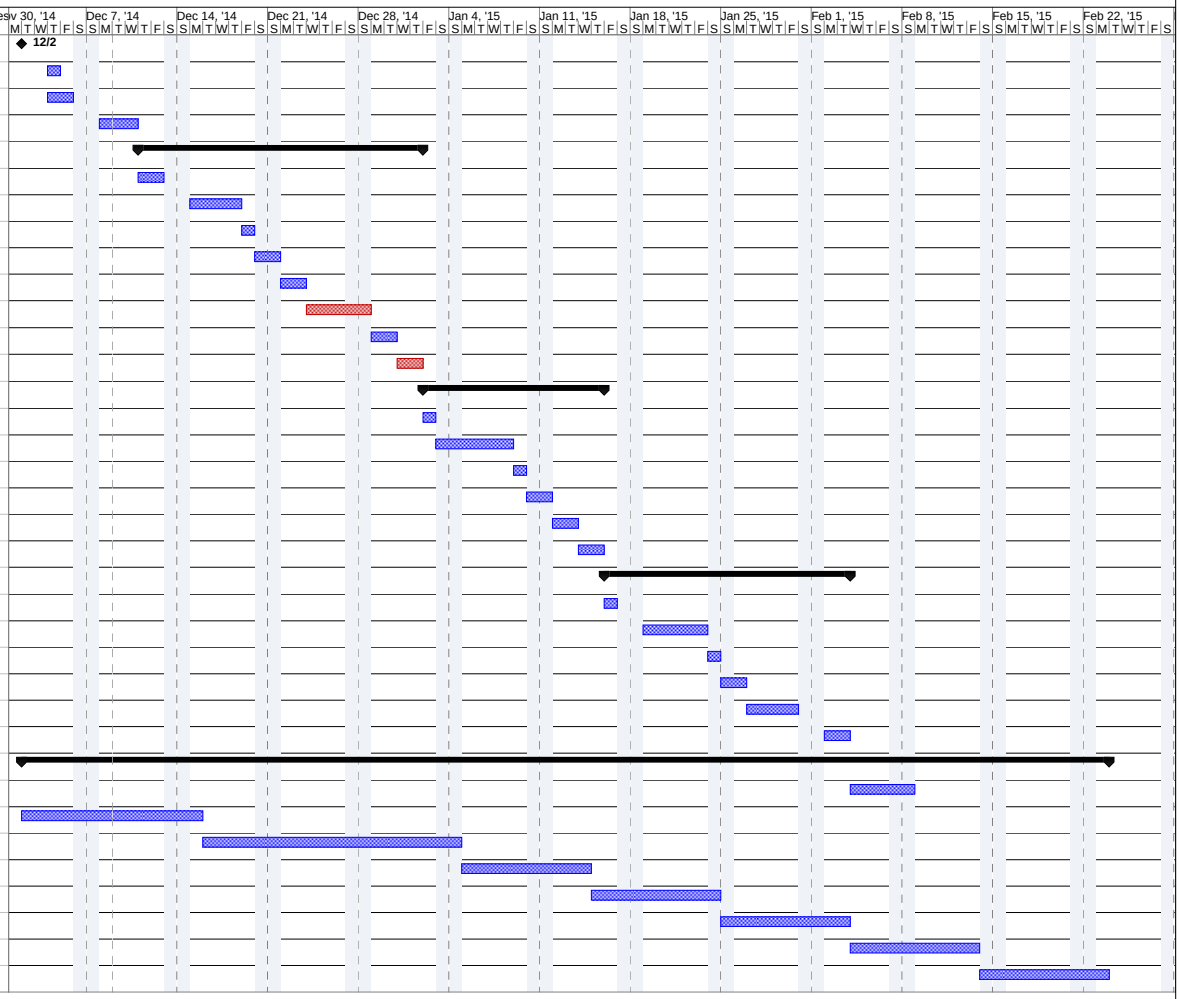

Project: EW005-EW006&636R schedu

Task		Rolled Up Milestone		Project Summary		Inactive Milestone		Manual Summary Rollup		External Tasks	
Milestone		Rolled Up Progress		Group By Summary		Inactive Summary		Manual Summary		External Milestone	
Summary		Split		Inactive Task		Manual Task		Start-only		Progress	
Rolled Up Task		External Tasks		Inactive Milestone		Duration-only		Finish-only		Deadline	
