ID	Task Name	Duration	Start	Finish
1	Mobilization	5 days	Mon 1/26/15	Fri 1/30/15
2	Prepare Road to W Berm	2 days	Tue 2/3/15	Wed 2/4/15
3	**Repair SE Berm**	**24 days**	**Thu 2/5/15**	**Tue 3/10/15**
4	Initial Stabilization	2 days	Thu 2/5/15	Fri 2/6/15
5	Place to Full Height	3 days	Thu 3/5/15	Mon 3/9/15
6	Final Grading	1 day	Tue 3/10/15	Tue 3/10/15
7	**Repair W Berm**	**20 days**	**Mon 2/9/15**	**Fri 3/6/15**
8	Placement of 1st lift	5 days	Mon 2/9/15	Fri 2/13/15
9	Placement of Clay	10 days	Thu 2/19/15	Wed 3/4/15
10	Final Grading	2 days	Thu 3/5/15	Fri 3/6/15
11	Preparation of Road from Borrow 2	3 days	Fri 2/13/15	Wed 2/18/15

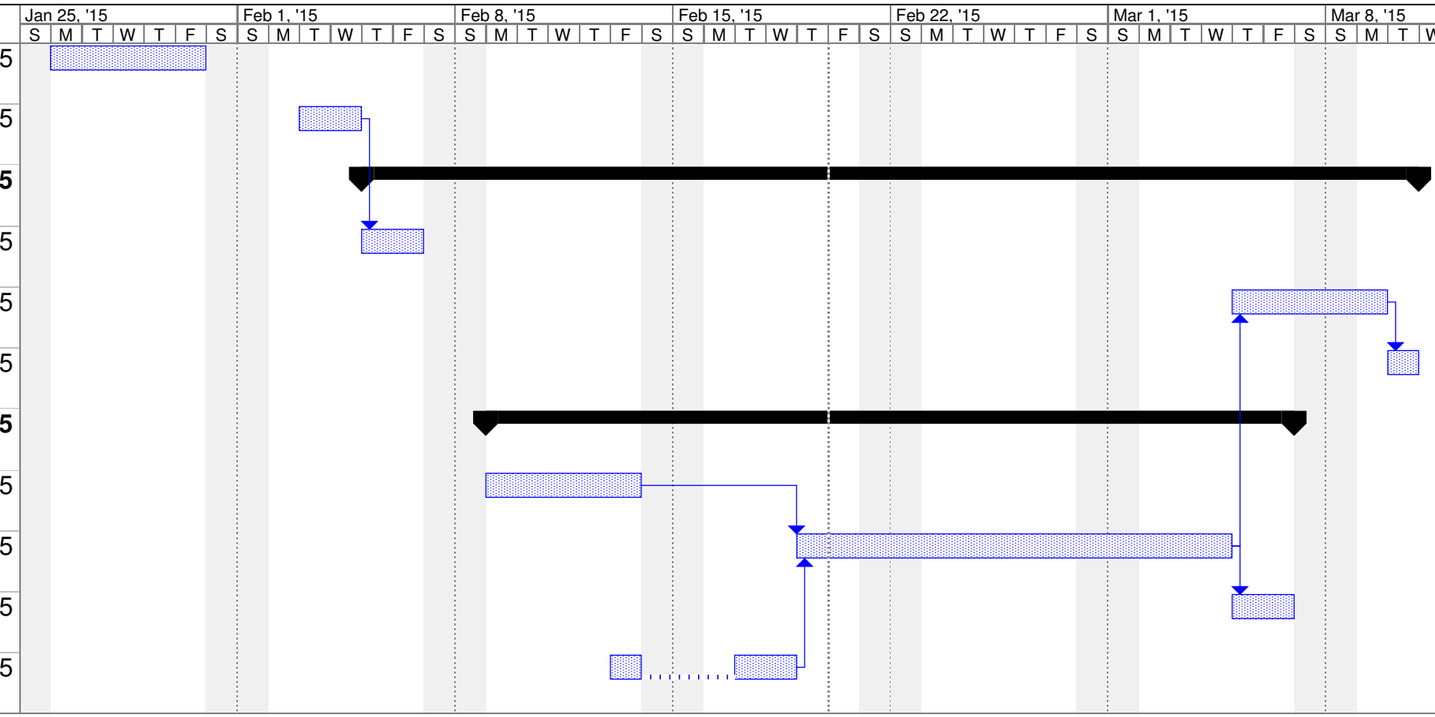

Pond 6 Berm Repair
Project: Anticipated Project
Date: Fri 2/20/15

Task | Progress | Summary | External Tasks | Deadline
Split | Milestone | Project Summary | External Milestone
